
		Contract No. HY/2019/14 New Wang Tong River Bridges 3-Month Rolling Programme													
識別碼	Task Name	·完成百;	工期	開始時間	完成時間	2021年11月				2021年12月					
						中旬	下旬		上旬	中旬	下旬	1	上旬	中旬	下
1	Submissions & Approval for Works within Wang Tong River (PS 1.93(1) (a)) DIA	79%	125 days	2021/7/5	2021/11/30										
2	Engineer's Design Review	73%	153 days	2021/6/19	2021/12/17			$\sim$	$\times$	$\times$	$\sim\sim\sim\sim\sim$	$\times\!\!\times\!\!\times$	$\times$	$\times$	73%
3	Cost Saving Design Proposal (Submission and Approval)	49%	120 days	2021/8/20	2022/1/13			x x		$\times$	* * * * * * *	XXXX		* * * * * *	* * * * * * *
4	Pre-drilling for CSD Piling Works (11 Holes)	76%	51 days	2021/9/13	2021/11/13					76%					
5	Submission of method statements and risk assessments of cofferdam works	45%	31 days	2021/10/15	2021/11/19						45%				
6	Submission of the proposed Sub-contractor for piling works	0%	15 days	2021/11/5	2021/11/22				$\times$		0%				
7	Submission of method statements and risk assessments of piling works	0%	35 days	2021/10/15	2021/11/24	$\times$		$\times$			0%	6			
8	Submission of the proposed Sub-contractor for structural steelworks	100%	5 days	2021/7/16	2021/7/21										
9	Submission of method statements and risk assessments of steelworks	0%	65 days	2021/10/15	2021/12/31	$\times$	*****	~~~~~		*****	~~~~~	$\times\!\!\times\!\!\times$		*****	~~~~~
10	Construction of cofferdams (for MP1, MP2 & MP3)	0%	30 days	2021/12/1	2022/1/7							Þ	~~~~~		~~~~~
11	MP1	0%	10 days	2021/12/1	2021/12/11								******	<u> </u> %	
12	MP2	0%	10 days	2021/12/13	2021/12/23										0%
13	MP3	0%	10 days	2021/12/24	2022/1/7										X
14	Mobilization Plants and Staging for Piling Works	0%	26 days	2021/12/13	2022/1/14										
15	Preliminary Piling (2 numbers) (2 Piles located at Pile MP2)	0%	15 days	2022/1/15	2022/2/4									//////	
16	Tension & Compression Load Test for Preliminary Piles	0%	52 days	2022/2/5	2022/4/7										
17	Submission of Shop Drawing for Structural Steel works and Approval	33%	76 days	2021/9/30	2021/12/31			XXX	*****	*****	*****	$\times$	~~~~~	*****	××××××
18	Fabrication of Structural Steelwork for Cycle bridges	0%	60 days	2022/1/3	2022/3/16			× ×							
19	Submit Bridge Bearings and Movement Joint for approval	0%	48 days	2022/1/3	2022/3/2										

	Critical	Task	Baseline	Milestone	•	Project Summary		Deadline
3-Month Rolling Programme Date: 20211105	Critical Split	 Split	 Baseline Split	, Summary Progress	s	External Tasks		
	Critical Progress	Task Progress	Baseline Milestone $\diamondsuit$	Summary	<b>—</b>	External Milestone	•	
				Page 1				

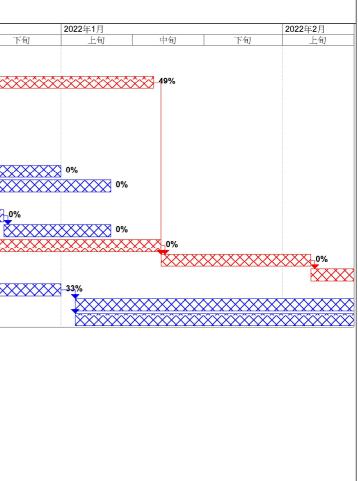

 $\mathcal{C}$
