Contract No. HY/2019/14 New Wang Tong River Bridges
3-Month Rolling Programme

識別碼	Task Name	完成百分	工期	開始時間	完成時間
1	Submissions & Approval for Works within Wang Tong River (PS 1.93(1) (a)) DIA	100%	125 days	2021/7/5	2021/11/30
2	Engineer's Design Review	100%	156 days	2021/6/19	2021/12/21
3	Cost Saving Design Proposal (Submission and Approval)	73%	150 days	2021/8/20	2022/2/21
4	Pre-drilling for CSD Piling Works (11 Holes)	100%	51 days	2021/9/13	2021/11/13
5	Submission of method statements and risk assessments of cofferdam works	97%	66 days	2021/10/15	2022/1/3
6	Submission of the proposed Sub-contractor for piling works	100%	15 days	2021/11/5	2021/11/22
7	Submission of method statements and risk assessments of piling works	65%	80 days	2021/10/15	2022/1/19
8	Submission of the proposed Sub-contractor for structural steelworks	100%	5 days	2021/7/16	2021/7/21
9	Submission of method statements and risk assessments of steelworks	60%	85 days	2021/10/15	2022/1/25
10	Inspection pit to Identify 300mm sewer location	21%	44 days	2021/11/26	2022/1/19
11	Existing watermain diversion near MP3	3%	40 days	2021/12/30	2022/2/18
12	Construction of cofferdams (for MP1, MP2 & MP3)	0%	18 days	2022/1/6	2022/1/26
13	MP2	0%	6 days	2022/1/6	2022/1/12
14	MP3 (Easten, Southen and Northen Sheetpile wall)	0%	5 days	2022/1/13	2022/1/18
15	MP3 (Westen Sheetpile wall after watermain diversion)	0%	3 days	2022/2/19	2022/2/22
16	MP1	0%	6 days	2022/2/22	2022/2/28
17	Mobilization Plants and Staging for Piling Works	0%	12 days	2022/2/23	2022/3/8
18	Preliminary Piling (2 numbers with 4 reaction pile) (at Pile Cap MP2)	0%	24 days	2022/3/9	2022/4/6
19	Tension & Compression Load Test for Preliminary Piles	0%	52 days	2022/4/7	2022/6/13
20	Main Piling at MP1, MP2 & MP3 (31 Numbers)	0%	62 days	2022/4/7	2022/6/24
21	Submission of Shop Drawing for Structural Steel works and Approval	75%	100 days	2021/9/30	2022/1/29
22	Fabrication of Structural Steelwork for Cycle bridges	0%	60 days	2022/1/31	2022/4/14
23	Submit Bridge Bearings and Movement Joint for approval	0%	48 days	2022/1/31	2022/3/30

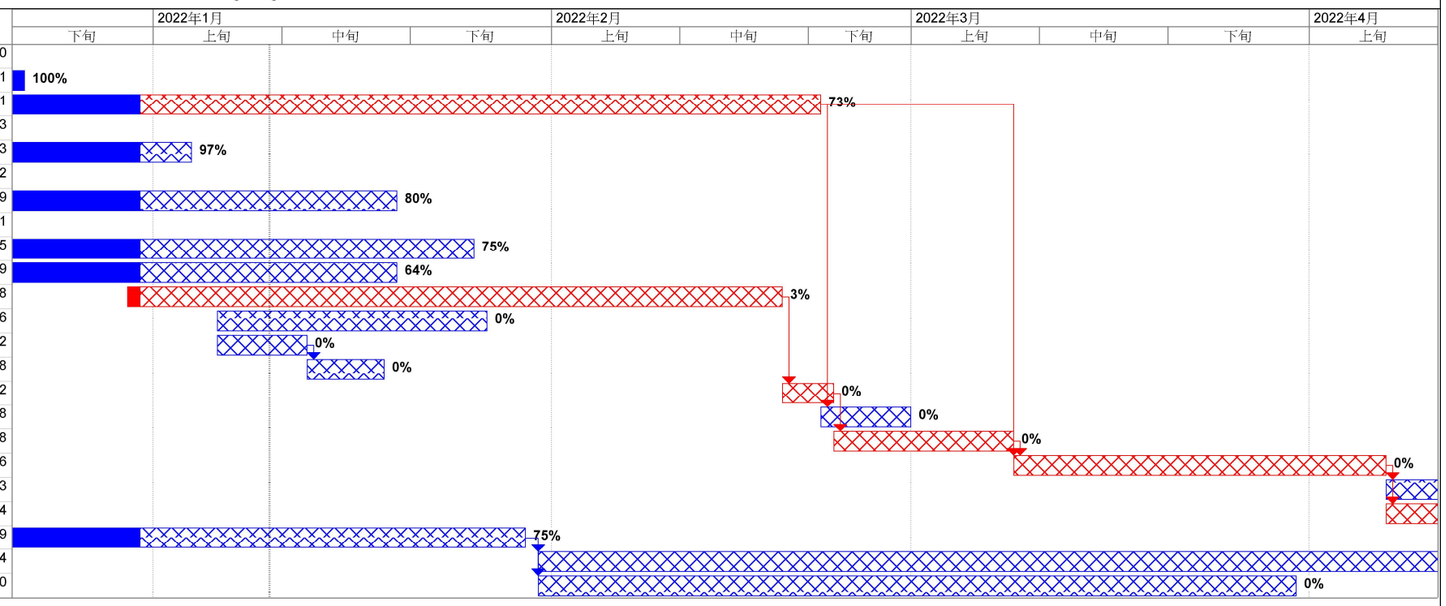

3-Month Rolling Programme
Date: 20220110

Critical
Critical Split
Critical Progress
Task
Split
Task Progress
Baseline
Baseline Split
Baseline Milestone
Milestone
Summary Progress
Summary
Project Summary
External Tasks
External Milestone
Deadline
