Contract No. HY/2019/14 New Wang Tong River Bridges
3-Month Rolling Programme

識別碼	Task Name	完成百	工期	開始時間	完成時間
1	Submissions & Approval for Works within Wang Tong River (PS 1.93(1) (a)) DIA	94%	80 days	2021/7/5	2021/10/7
2	Engineer's Design Review	58%	153 days	2021/6/19	2021/12/17
3	Cost Saving Design Proposal (Submission and Approval)	50%	130 days	2021/7/16	2021/12/17
4	Tree Felling	100%	39 days	2021/7/12	2021/8/25
5	Pre-drilling for CSD Piling Works (11 Holes)	34%	44 days	2021/9/13	2021/11/5
6	Submission of the proposed Sub-contractor for cofferdam works	0%	5 days	2021/10/8	2021/10/13
7	Submission of method statements and risk assessments of cofferdam works	0%	15 days	2021/10/15	2021/11/1
8	Submission of the proposed Sub-contractor for piling works	0%	5 days	2021/10/8	2021/10/13
9	Submission of method statements and risk assessments of piling works	0%	15 days	2021/10/15	2021/11/1
10	Submission of the proposed Sub-contractor for structural steelworks	100%	5 days	2021/7/16	2021/7/21
11	Submission of method statements and risk assessments of steelworks	0%	15 days	2021/10/15	2021/11/1
12	Sub-contracting Piling and Structure Steel Works	100%	10 days	2021/7/22	2021/8/2
13	Construction of cofferdams (for MP1, MP2 & MP3)	0%	30 days	2021/11/6	2021/12/10
14	MP1	0%	10 days	2021/11/6	2021/11/17
15	MP2	0%	10 days	2021/11/18	2021/11/29
16	MP3	0%	10 days	2021/11/30	2021/12/10
17	Mobilization Plants and Staging for Piling Works	0%	26 days	2021/11/18	2021/12/17
18	Preliminary Piling (2 numbers) (2 Piles located at Pile MP2)	0%	15 days	2021/12/18	2022/1/7
19	Tension & Compression Load Test for Preliminary Piles	0%	52 days	2022/1/8	2022/3/12
20	Submission of Shop Drawing for Structural Steel works and Approval	0%	52 days	2021/9/30	2021/12/1
21	Fabrication of Structural Steelwork for two bridges (106 tonne)	0%	48 days	2021/12/2	2022/1/29
22	Submit Bridge Bearings and Movement Joint for approval	0%	48 days	2021/12/2	2022/1/29

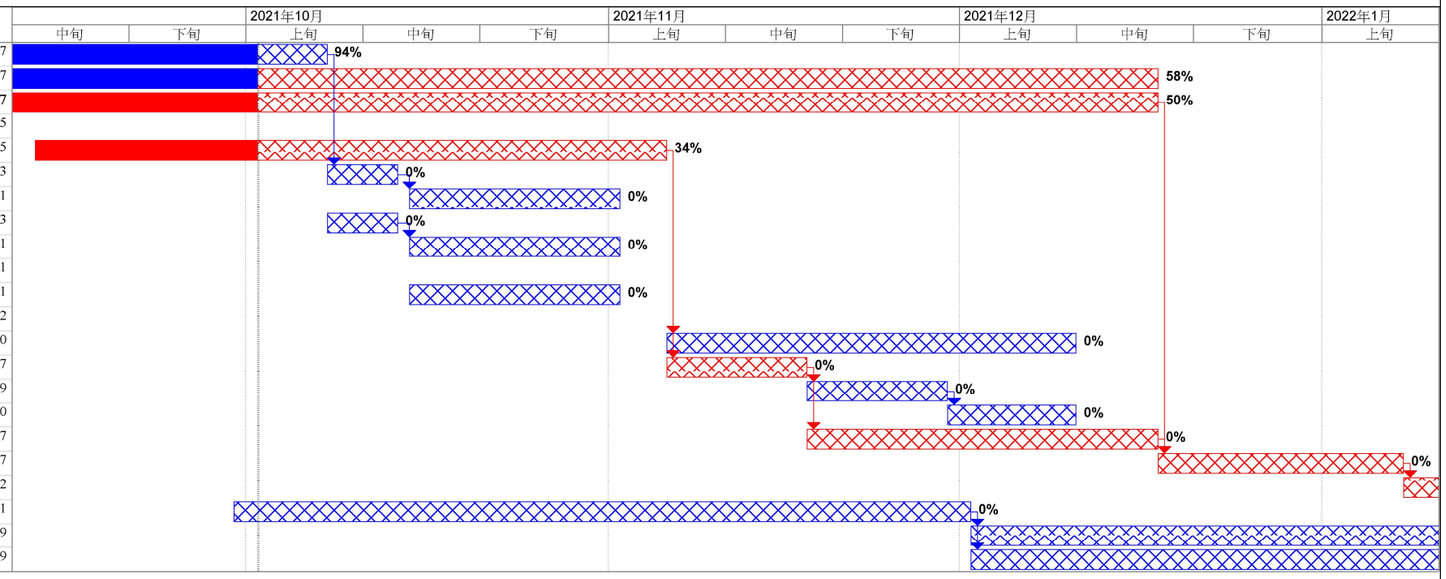

3-Month Rolling Programme (E)
Date: 20210930

Critical | Task | Baseline | Milestone | Project Summary | Deadline
Critical Split | Split | Baseline Split | Summary Progress | External Tasks
Critical Progress | Task Progress | Baseline Milestone | Summary | External Milestone
